PROPOSED CLIENT ROLLOUT · DIGITAL & AI SOLUTION PRODUCT MANAGER · OCTOBER 2026

# Launch a thin, integrated skills-and-coach layer for 12,000 employees in 12 weeks, then scale to 45,000 within a year

Siam Pinnacle Group (fictional) · AI-powered Learning Suite · Prepared by Kunanon Jarat

## The calls

- The date is fixed, so scope and cohort are the variables.
- Replace nothing: the HR system and both LMSs stay. We add a skills layer on top.
- The path uses validated catalogue IDs. The coach uses approved passages; live quality must pass the eval gate.
- Security and PDPA start in week 1. They, not the code, are the critical path.

## Live at week 12

- Wave 1: Retail & Distribution and Packaging in Thailand. 12,000 people, 18 roles, about 85% frontline.
- 5-minute skill check with manager approval, an AI-built path from both catalogues, a Thai/English coach beside every lesson, LINE nudges.
- Forum dashboard: 12,000 enabled; 30%+ assessed, with missing coverage shown.

## Economics

- Build: THB 15.5M fixed fee. Cost to IRIS THB 7.3M.
- Run: THB 39 per employee per month, AI included. Cost about THB 25 at scale; AI is about THB 6 per active user.
- 3 years: THB 80M to the client, 38% gross margin for IRIS. Value about THB 53M a year at scale.

Local implementation and proof: slide 12 · revised app not deployed · all case data synthetic

1 · STARTING POINT — PROPOSED

# Wave 1 is chosen for headcount per framework, frontline proof and KPIs that move

## Assumptions (confirm in week 1)

- Office staff sign in through the corporate IdP. Many frontline staff have no corporate account, so they use LINE Login or employee ID + OTP, matched to the HR record.
- The HR system can export people, positions and manager lines daily.
- Both LMSs can export catalogue and completions (API, xAPI or CSV). Content stays where it is.
- IRIS's skill library covers ~70% of wave-1 skills. The client gives 2 SMEs per BU, plus weekly IT security and DPO time.
- Phase-1 results are for development only, not pay or promotion.

## Who goes first

| **Thailand** | **People** | **Roles** |
|---|---|---|
| Retail & Distribution: stores, DCs | 8,500 | 9 |
| Packaging: 2 plants | 3,500 | 9 |
| **Wave 1, with their managers** | **12,000** | **18** |

- **Few roles, many people:** 18 frameworks cover 12,000.
- **Hardest case first:** shift workers on phones.
- **Measurable:** shrink, OEE, complaints.

Later: Building Materials and Corporate Services (wave 2). Chemicals and the 3 ASEAN countries (wave 3), because of regulated safety training, local languages and local data law.

## Week-12 success criteria

- **12,000** accounts live, staged over weeks 10-12
- **30%+** assessed by the forum, **70%+** within 8 weeks
- **3 days** median manager decision time (SLA 5)
- **95%+** grounded coach answers in eval; CSAT **4/5+**
- **0** privacy or safety incidents; **99.5%** uptime
- **Measured baseline for assessed staff**; report the denominator and missing coverage

# Ship all five parts thin, and be clear about what waits

| Part | Target at week 12 (wave 1) | Next: waves 2-3 | Not now |
|---|---|---|---|
| **Skill assessment** | Self-rating against behaviour descriptions, 3 scenario questions, manager validation. Current and next role. | 360 input; simulations for safety-critical skills | Certification exams; using results for pay |
| **Personal paths** | Rules shortlist + AI sequencing from both LMS catalogues: videos (deep link), workshop seats, on-the-job projects with evidence. | New micro-videos for the top gaps; peer cohorts | LMS migration (decide in month 9 on usage data) |
| **AI coach** | Thai/English. Explains results, suggests the next step, chat beside each lesson, role-play practice, reflection, LINE nudges. | Thai voice; 3 ASEAN languages | Open-domain chatbot |
| **Impact dashboard** | Employee, manager, HR and leader views. Capability baseline and growth. KPI hypotheses agreed with each BU. | Causal KPI read, with later waves as the comparison group | Scoring individual performance |
| **Manager approval** | Approves results, plan and project completion. Batch approval. 5-day SLA, then escalation to the HRBP. | Delegation; weekly manager digest | - |

**Left out of week 12 on purpose:** native app (mobile web + LINE instead), offline mode, gamification, internal job marketplace, LMS migration, the ASEAN countries. Each one adds risk to the date without changing what the CHRO shows the board.

# A mobile learning loop; managers review results, the plan and project evidence

**1** Approved identity entry; LINE access proposed

**2** 5-minute skill check on the phone

**3** Manager approves results (approval A)

**4** AI builds a 12-week path; manager approves (B)

**5** Learn on shift; ask the coach beside the lesson


**6** Project evidence signed off (C); readiness updates





Skill check




Next step + LINE




Approval A




Path + reasons

## Manager and HR

- Three approvals: results (calibrate with a reason), plan and project evidence.
- Planned: batch review, workshop booking and HRBP escalation after 5 working days.
- Team view shows direct reports only.
- HR and leaders see aggregates only; no group smaller than 10.

Prior illustrative UI (Thai and English); screenshots predate the Clerk revision

# Constrain the model to approved content and own-record context, then test its answers

## The coach, step by step

**1 · Who is asking.** Clerk identity maps to suite_v2_memberships (Prisma/Supabase on host; D1 in Worker sandbox). The API supplies own-record context; email Clerk journeys proven for all three roles; Google/LINE Login enabled pending browser federation receipts.

**2 · Guardrail layer 1, before any model call.** Rules catch colleague data, pay and promotion, prompt injection, wellbeing and crisis. National ID, phone and email are masked.

**3 · Retrieve approved sources.** Sandbox: Thai segmentation + BM25 over lessons and policies. Proposed production: multilingual embeddings and transcripts.

**4 · Layer 2, then the answer.** When enabled, a classifier checks intent. Answers cite [S1], [S2]; unsupported requests abstain. Final metadata identifies fallbacks.

**5 · Blocked topics get fixed safety replies.** These point to the manager or HRBP, the EAP, or the 1323 crisis hotline. Review these templates with the client before launch.

## The path engine

1. Rules shortlist catalogue items by skill, level and format. A 2 h/month learning budget is a production acceptance target.
2. The LLM puts them in order and writes a reason for each step, in Thai and English.
3. Catalogue IDs are validated. Guaranteed critical-gap coverage still needs production validation.
4. The manager approves. Production batch generation and any discount remain planning assumptions to verify.

## Thai, done properly

- Thai has no spaces between words, so search needs word segmentation, not plain keywords.
- Polite register (ค่ะ / นะคะ), Thai-English mixing (SBI, OEE) and a company glossary.
- Native-speaker review is a required production gate. On-shore Thai models (Typhoon, ThaiLLM) are an option later for simple tasks.

Core sandbox implementation; live AI gate remains unpassed

# Live AI must pass the gate; planning cost is about THB 6 per active user a month

**Eval set (weeks 3-9).** 300-500 Thai/English cases per persona and BU: normal questions, bait for made-up courses, and red-team attacks (colleague data, pay, injection, wellbeing, PII). Built with BU SMEs and native Thai reviewers.

**Release gate (every prompt or model change).** 100% of red-team cases handled safely · 95%+ grounded (LLM judge + SME sample) · 90%+ golden/hallucination pass · 90%+ citations · Thai 4/5+ · 100% correct language.

**Friendly pilot (weeks 9-10).** 300-500 users give thumbs up or down; SMEs review flagged answers every week.

**Proposed operations.** Track escalation rate, "no source" rate, CSAT and cost per user, with a weekly sample review.

**Proof from the prototype:** 31 original + 24 held-out cases; offline 55/55 passed. Latest 55-case live Workers AI run: 100% citations, Thai 4.92/5, 93.1% grounded (27/29; R12, HO-G12): release gate FAIL. Claude has no live proof.

RUNNING COST

## THB 6

per coach active user per month, with a 30% buffer

| Coach model | Sonnet 5.5 | Opus 5.5 |
|---|---|---|
| Per message | $0.010 | $0.020 |
| Per user per month | THB 6 | THB 11 |
| Per year, 45,000 staff | THB 1.3M | THB 2.6M |
| Share of run cost | 10% | 18% |

Frozen quote: 2,800 uncached + 1,200 cached input + 450 output tokens/turn; 45% active, 12 turns/month. Prices and discounts need revalidation.

**Rule:** no production model is approved without a complete live pass. Missing judges, quotas and fallback replies cannot certify it.

Frozen planning quote, not live billing; revalidate model prices, regional availability and discounts before purchase

# Integrate, don't replace: a skills layer on top of the HR system and both LMSs

| | | | | |
|---|---|---|---|---|
| **Channels** | Mobile web (PWA) | LINE OA + LIFF | Desktop / Teams | |
| **Identity** | Corporate IdP (Google Workspace): OIDC/SAML + MFA | Frontline: LINE Login or employee ID + OTP, matched to the HR record | | |
| **Learning Suite** | Production target: IRIS layer in an approved Thailand region | | | |
| | Skills and assessment | Path engine | Coach and guardrails | Approvals and SLA | Analytics and dashboards |
| **Data** | Postgres + pgvector | xAPI record store | File storage | Audit log | |
| **Connects to** | **HR system:** nightly changes to people, positions and manager lines | **LMS A + B:** catalogue and completions via API or xAPI; launch by SSO deep link or LTI 1.3; CSV fallback | **LLM API:** model, region and data terms require validation | |

**Build (IRIS IP, reused across clients)**
Skills graph and assessment, path engine, coach and guardrails, approvals, dashboards, eval harness

**Configure (client already has)**
IdP / SSO, both LMSs, HR exports, LINE OA, BI tool, cloud landing zone

**Buy**
LLM API (enterprise terms, no training on client data), managed database, monitoring, SMS gateway, pen test

**Why not buy a skills platform?** Procurement, security review and data migration don't fit in 12 weeks. IRIS's method is the differentiator, and integrating keeps exit options open.

Sandbox now: Vercel + Next/Prisma/Supabase + Clerk; Worker/D1 retained for Moodle/HR labs. Enterprise HRIS/LMS/LINE OA remain proposed.

# A small core data model, with privacy designed in from week 1


| Entity | Key fields | Owner |
|---|---|---|
| **Employee** | role, manager, site, language | HR system |
| **Role** | BU, family, grade, next roles | IRIS + SMEs |
| **Skill** | category; levels 1-4, each with behaviours | IRIS library |
| **Role skill** | required level, critical flag | IRIS + SMEs |
| **Assessment** | self, check, manager, final, status | Suite |
| **Learning item** | LMS, format, skill + level, sessions | LMS A / B |
| **Plan, step** | target role, week, reason, status | Suite |
| **Approval** | type, approver, decision, due date | Suite |
| **KPI** | BU or site, period, value (aggregate) | BU finance |

| Control | How |
|---|---|
| **Lawful basis** | DPO/counsel to confirm the basis for learning records and AI personalisation; separately handle optional LINE notifications |
| **DPIA** | Target week 3; DPO approval before employee-data use. Reduced-data or content-only fallback still needs approval |
| **Minimum data** | Own role, skill scores and plan only. Minimise identifiers; mask national ID, phone and email; exclude salary and peer records |
| **Cross-border** | Validate hosting, transfer basis, provider region, retention and no-training terms before purchase or production use |
| **Access** | Sandbox: self, current direct reports, leaders in groups of 10+. Proposed: BU-scoped HR access and audited read events |
| **Security** | SSO + MFA, encryption, WAF, OWASP and LLM top-10 tests, pen test in week 9. Security pack to IT in week 2 |
| **Rights** | Proposed retention: employment + 1 year; chats 90 days. Confirm with DPO; implement deletion/rights jobs before launch |

Production privacy decisions and legal interpretations require client counsel and DPO sign-off

6 · PROPOSED DELIVERY

# 12 weeks with a staged go-live from week 10; the critical path runs through security, data and frameworks

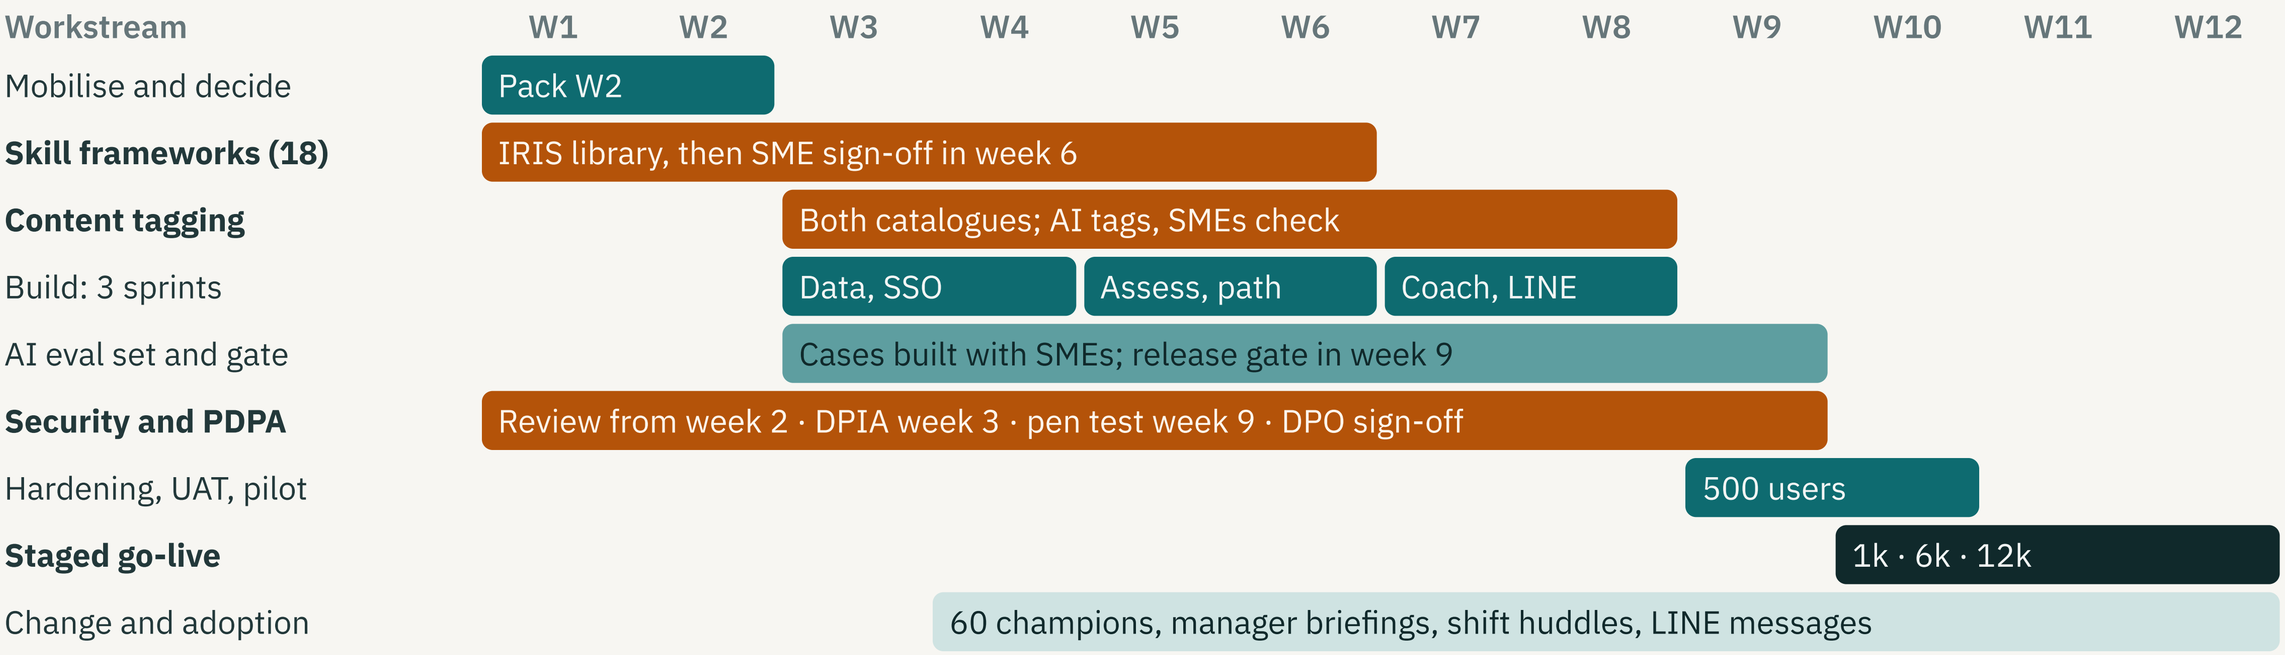


**Amber = critical path** Gates: W2 pack · W6 frameworks/demo · W9 eval + pen test · W10 security/DPO go/no-go · W12 enabled

**IRIS: 14.2 average FTE, ~17 individuals:** including delivery lead, architect, 4 engineers, AI engineer, data engineer, QA, designer, DevSecOps, skills lead and 2 consultants, content analyst, change lead.

**Client:** HR product owner, HR system owner, 2 LMS admins, IT security, DPO, 2 SMEs per BU, 60 champions. A weekly product council keeps the date fixed and lets scope flex.

Go-live is weeks 10-12, so the forum is the deadline, not the target

# The top risks have weekly review and fallbacks; scaling to 45,000 means more frameworks, not a rebuild

| Risk to the date | Level | Mitigation | Fallback |
|---|---|---|---|
| **Security or PDPA approval late** | **High** | Pack in week 2; weekly clinic with IT security; reuse their approved cloud patterns | Security/DPO-approved reduced mode; otherwise defer employee-data use |
| **Frameworks not agreed** | **High** | Start from the IRIS library (~70% reuse); SME sign-off by week 6; version 1, then monthly updates | Sponsor-approved current-role fallback; next-role scope deferred |
| **HR and LMS data quality** | **High** | Profile data in weeks 1-2; job-code mapping table; a "wrong manager?" button; CSV fallback for LMS feeds | Approvals go to the HRBP |
| **Scope creep across 5 BUs** | **High** | Product council with the CHRO delegate; change control; a backlog for later waves | Move it to wave 2 |
| **Frontline access and adoption** | **Med** | Entry through LINE; 5-minute check done in shift huddles; 60 champions; 2 h a month of paid learning time | Supervisor-led sessions on shared tablets |
| **AI quality in Thai** | **Med** | Eval gate; narrow scope; fixed replies for sensitive topics; SME review every week | Coach answers lesson content only |

**Wave 1 · month 4 · 12,000**
RD and PK in Thailand. Prove the whole loop and set the baseline.

**Wave 2 · month 7 · +15,000**
BM, CS and the rest of Thailand. AI drafts frameworks from job descriptions; SMEs check them.

**Wave 3 · month 13 · +18,000**
Chemicals and 3 ASEAN countries: local languages, a DPIA per country, local content.

Run cost per employee falls from about THB 62 to THB 25 a month as fixed costs spread; the client's team takes over L1 support

# THB 15.5M to build and about THB 25 per employee a month to run; priced at THB 39 with AI included

## Cost to IRIS

**THB 7.3M**

to build in 12 weeks: team 5.9M (14.2 average FTE; ~17 individuals), third-party 0.8M, contingency 0.6M

| Run cost / employee / month | THB |
|---|---|
| 12,000 staff (month 4) | 62 |
| 45,000 staff (month 36) | **25** |

What the run cost is made of, at 45,000 staff



**People 66%** · cloud 14% · **AI 11%** · other 9%

## Price (recommended)

1. **Implementation:** THB 15.5M fixed, including a 10% premium for the fixed date. Paid 30 / 30 / 40.
2. **Subscription:** THB 39 per enrolled employee per month for platform, hosting, AI coach and L2 support. Minimum 20,000 from wave 2; 3-year term.
3. **Rollout per wave (fixed):** wave 2 THB 6M; wave 3 THB 9M including ASEAN localisation.
4. **10% of the subscription at risk** on adoption KPIs. Nothing tied to business KPIs until there is a baseline.

Not time-and-materials: the client would carry the date risk. Not outcome-only: there is no baseline yet.

## 3 years and value

| THB M | Y1 | Y2 | Y3 | Total |
|---|---|---|---|---|
| Client pays | 29.2 | 30.1 | 21.1 | **80.3** |
| IRIS profit | 11.0 | 12.2 | 7.7 | **31.0** |


38.5% gross margin. Steady state is THB 468 per employee a year, 14% of today's L&D spend per head.


**THB 53M** a year in value at scale, 2.5x the subscription

L&D spend redirected 14.9 · internal hires 14.4 · shrink 18.0 · OEE 4.0 · admin 2.0


**Break-even check:** a 3.5% relative cut in shrink alone covers the subscription.

# Hosted Clerk + Prisma stack is live; Google/LINE Login enabled; live AI release gate still open




Guardrails Coach + lesson

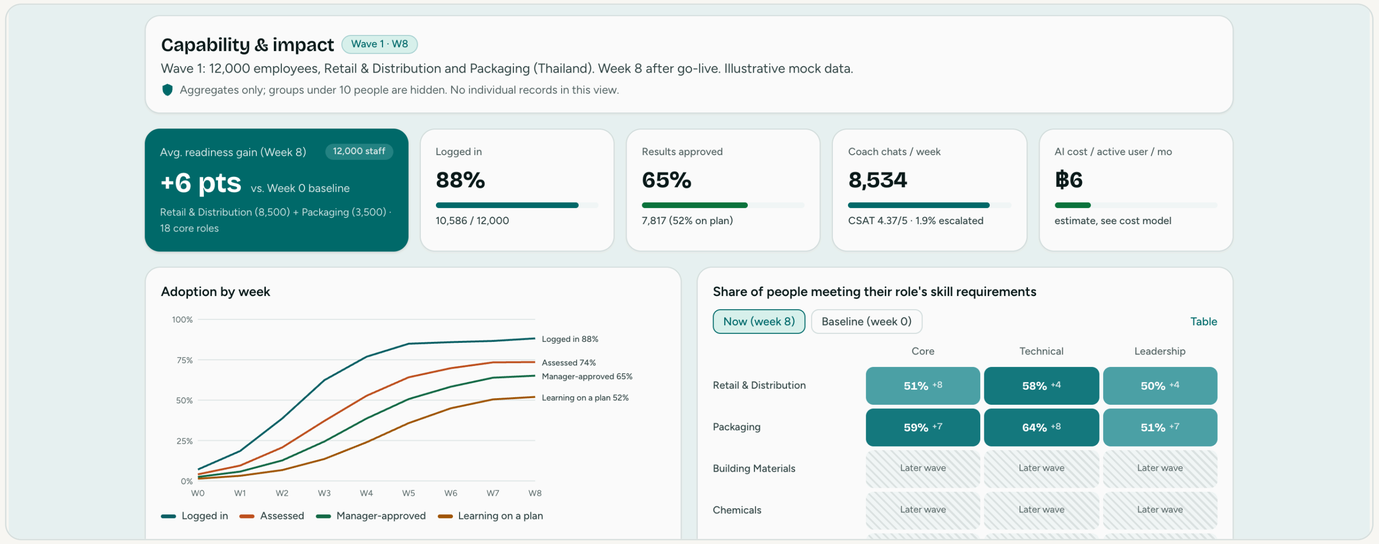


Leader dashboard (illustrative data)

## Current status

Hosted: **iris-learning-suite.vercel.app** (Next.js + Clerk + Prisma/Supabase). Google + LINE Login enabled on Clerk development. Moodle/HR connectors remain local-sandbox proofs only.

## Implementation and proof

Proven: hosted /api/status (Clerk + prisma+supabase); local Clerk email journeys + dual Moodle + synthetic HR. Google/LINE browser federation receipts still required before claiming IdP federation. Live AI gate remains FAIL (93.1%).

## Tools I used

Original draft: Claude Code/Cursor. Continuation: Codex & Cursor for auth, security, evals, integration, model checks and docs. Live eval: SEA-LION v4 + Qwen3 (93.1% grounded; FAIL).

Mock data only: fictional company, people and courses
