PROPOSED CLIENT ROLLOUT · DIGITAL & AI SOLUTION PRODUCT MANAGER · OCTOBER 2026

Launch a thin, integrated skills-and-coach layer for 12,000 employees in 12 weeks, then scale to 45,000 within a year

Siam Pinnacle Group (fictional) · AI-powered Learning Suite · Prepared by Kunanon Jarat

The calls

- The date is fixed, so scope and cohort are the variables.
- Replace nothing: the HR system and both LMSs stay. We add a skills layer on top.
- The path uses validated catalogue IDs. The coach uses approved passages; live quality must pass the eval gate.
- Security and PDPA start in week 1. They, not the code, are the critical path.

Live at week 12

- Wave 1: Retail & Distribution and Packaging in Thailand. 12,000 people, 18 roles, about 85% frontline.
- 5-minute skill check with manager approval, an AI-built path from both catalogues, a Thai/English coach beside every lesson, LINE nudges.
- Forum dashboard: 12,000 enabled; 30%+ assessed, with missing coverage shown.

Economics

- Build: THB 15.5M fixed fee. Cost to IRIS THB 7.3M.
- Run: THB 39 per employee per month, AI included. Cost about THB 25 at scale; AI is about THB 6 per active user.
- 3 years: THB 80M to the client, 38% gross margin for IRIS. Value about THB 53M a year at scale.

Wave 1 is chosen for headcount per framework, frontline proof and KPIs that move

Assumptions (confirm in week 1)

- Office staff sign in through the corporate IdP. Many frontline staff have no corporate account, so they use LINE Login or employee ID + OTP, matched to the HR record.
- The HR system can export people, positions and manager lines daily.
- Both LMSs can export catalogue and completions (API, xAPI or CSV). Content stays where it is.
- IRIS's skill library covers ~70% of wave-1 skills. The client gives 2 SMEs per BU, plus weekly IT security and DPO time.
- Phase-1 results are for development only, not pay or promotion.

Who goes first

Thailand	People	Roles
Retail & Distribution: stores, DCs	8,500	9
Packaging: 2 plants	3,500	9
Wave 1, with their managers	**12,000**	**18**

- **Few roles, many people:** 18 frameworks cover 12,000.
- **Hardest case first:** shift workers on phones.
- **Measurable:** shrink, OEE, complaints.

Later: Building Materials and Corporate Services (wave 2). Chemicals and the 3 ASEAN countries (wave 3), because of

Week-12 success criteria

- **12,000** accounts live, staged over weeks 10-12
- **30%+** assessed by the forum, **70%+** within 8 weeks
- **3 days** median manager decision time (SLA 5)
- **95%+** grounded coach answers in eval; CSAT **4/5+**
- **0** privacy or safety incidents; **99.5%** uptime
- **Measured baseline for assessed staff**; report the denominator and missing coverage

Ship all five parts thin, and be clear about what waits

Part	Target at week 12 (wave 1)	Next: waves 2-3	Not now
Skill assessment	Self-rating against behaviour descriptions, 3 scenario questions, manager validation. Current and next role.	360 input; simulations for safety-critical skills	Certification exams; using results for pay
Personal paths	Rules shortlist + AI sequencing from both LMS catalogues: videos (deep link), workshop seats, on-the-job projects with evidence.	New micro-videos for the top gaps; peer cohorts	LMS migration (decide in month 9 on usage data)
AI coach	Thai/English. Explains results, suggests the next step, chat beside each lesson, role-play practice, reflection, LINE nudges.	Thai voice; 3 ASEAN languages	Open-domain chatbot
Impact dashboard	Employee, manager, HR and leader views. Capability baseline and growth. KPI hypotheses agreed with each BU.	Causal KPI read, with later waves as the comparison group	Scoring individual performance
Manager approval	Approves results, plan and project completion. Batch approval. 5-day SLA, then escalation to the HRBP.	Delegation; weekly manager digest	-

Left out of week 12 on purpose: native app (mobile web + LINE instead), offline mode, gamification, internal job marketplace, LMS migration, the ASEAN countries. Each one adds risk to the date without changing what the CHRO shows the board.

A mobile learning loop; managers review results, the plan and project evidence

1 Approved identity entry; LINE access proposed


2 5-minute skill check on the phone

3 Manager approves results (approval A)


4 AI builds a 12-week path; manager approves (B)


5 Learn on shift; ask the coach beside the lesson

6 Project evidence signed off (C); readiness updates


Prior illustrative UI: Skill check screen in Thai, choosing a level by behaviour description


Prior illustrative UI: Employee home screen in Thai with next step and LINE nudge preview


Prior illustrative UI: Manager approval screen showing self, quiz and final levels with adjust buttons


Prior illustrative UI: AI-built learning path with a reason for every step

Manager and HR

- Three approvals: results (calibrate with a reason), plan and project evidence.
- Planned: batch review, workshop booking and HRBP escalation after 5 working days.
- Team view shows direct reports only.
- HR and leaders see aggregates only; no group smaller than 10.

Prior illustrative UI (Thai and English); screenshots predate the Clerk revision

Skill check

Next step + LINE

Approval A

Path + reasons

Constrain the model to approved content and own-record context, then test its answers

The coach, step by step

1 · Who is asking. Clerk identity maps to suite_v2_memberships (Prisma/Supabase on host; D1 in Worker sandbox). The API supplies own-record context; email Clerk journeys proven for all three roles; Google/LINE Login enabled pending browser federation receipts.

2 · Guardrail layer 1, before any model call. Rules catch colleague data, pay and promotion, prompt injection, wellbeing and crisis. National ID, phone and email are masked.

3 · Retrieve approved sources. Sandbox: Thai segmentation + BM25 over lessons and policies. Proposed production: multilingual embeddings and transcripts.

The path engine

1. Rules shortlist catalogue items by skill, level and format. A 2 h/month learning budget is a production acceptance target.
2. The LLM puts them in order and writes a reason for each step, in Thai and English.
3. Catalogue IDs are validated. Guaranteed critical-gap coverage still needs production validation.
4. The manager approves. Production batch generation and any discount remain planning assumptions to verify.

Thai, done properly

- Thai has no spaces between words, so search needs word segmentation, not plain keywords.

Core sandbox implementation; live AI gate remains unpassed

Live AI must pass the gate; planning cost is about THB 6 per active user a month

Eval set (weeks 3-9). 300-500 Thai/English cases per persona and BU: normal questions, bait for made-up courses, and red-team attacks (colleague data, pay, injection, wellbeing, PII). Built with BU SMEs and native Thai reviewers.

Release gate (every prompt or model change). 100% of red-team cases handled safely · 95%+ grounded (LLM judge + SME sample) · 90%+ golden/hallucination pass · 90%+ citations · Thai 4/5+ · 100% correct language.

Friendly pilot (weeks 9-10). 300-500 users give thumbs up or down; SMEs review flagged answers every week.

Proposed operations. Track escalation rate, "no source" rate, CSAT and cost per user, with a weekly sample review.

RUNNING COST


THB 6 per coach active user per month, with a 30% buffer

Coach model	Sonnet 5.5	Opus 5.5
Per message	$0.010	$0.020
Per user per month	THB 6	THB 11
Per year, 45,000 staff	THB 1.3M	THB 2.6M
Share of run cost	10%	18%

Frozen quote: 2,800 uncached + 1,200 cached input + 450 output tokens/turn; 45% active, 12 turns/month. Prices and discounts

Frozen planning quote; must be live-validate model prices, regional availability and discounts before purchase

Integrate, don't replace: a skills layer on top of the HR system and both LMSs

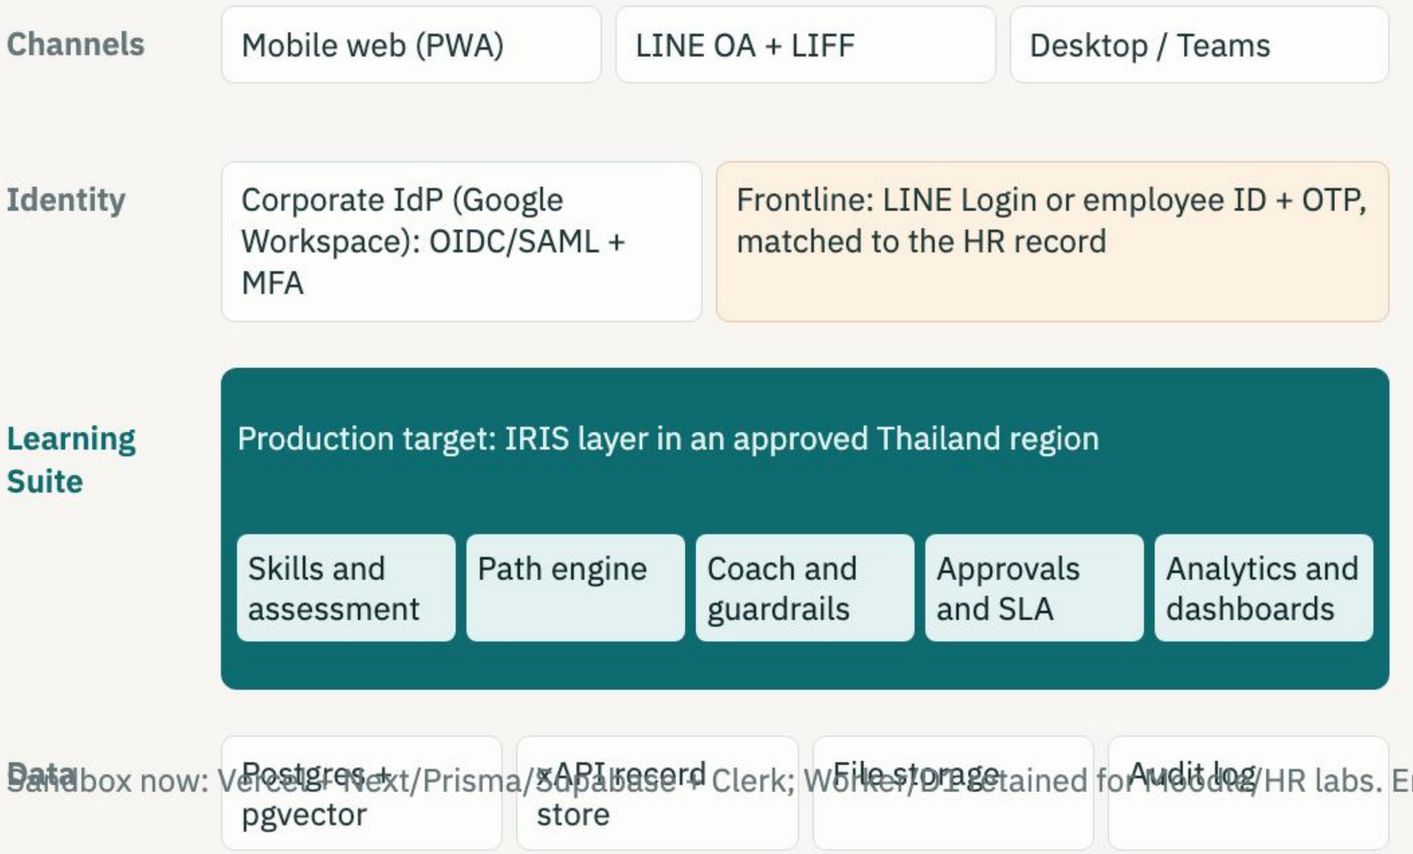

Build (IRIS IP, reused across clients)

Skills graph and assessment, path engine, coach and guardrails, approvals, dashboards, eval harness

Configure (client already has)

IdP / SSO, both LMSs, HR exports, LINE OA, BI tool, cloud landing zone

Buy

LLM API (enterprise terms, no training on client data), managed database, monitoring, SMS gateway, pen test

Sandbox now: Vercel + Next/Prisma/Supabase + Clerk; Worker/D1 retained for Moodle/HR labs. Enterprise HRIS/LMS/LINE OA remain proposed.


A small core data model, with privacy designed in from week 1

Entity	Key fields	Owner
Employee	role, manager, site, language	HR system
Role	BU, family, grade, next roles	IRIS + SMEs
Skill	category; levels 1-4, each with behaviours	IRIS library
Role skill	required level, critical flag	IRIS + SMEs
Assessment	self, check, manager, final, status	Suite
Learning item	LMS, format, skill + level, sessions	LMS A / B
Plan, step	target role, week, reason, status	Suite
Approval	type, approver, decision, due date	Suite
KPI	BU or site, period, value (aggregate)	BU finance

Control	How
Lawful basis	DPO/counsel to confirm the basis for learning records and AI personalisation; separately handle optional LINE notifications
DPIA	Target week 3; DPO approval before employee-data use. Reduced-data or content-only fallback still needs approval
Minimum data	Own role, skill scores and plan only. Minimise identifiers; mask national ID, phone and email; exclude salary and peer records
Cross-border	Validate hosting, transfer basis, provider region, retention and no-training terms before purchase or production use
Access	Sandbox: self, current direct reports, leaders in groups of 10+. Proposed: BU-scoped HR access and audited read events
Security	SSO + MFA, encryption, WAF, OWASP and LLM top-10 tests, pen test in week 9. Security pack to IT in week 2
Rights	Proposed retention: employment + 1 year; chats 90 days. Confirm with DPO; implement deletion/rights jobs before launch

Production privacy decisions and legal interpretations require client counsel and DPO sign-off

12 weeks with a staged go-live from week 10; the critical path runs through security, data and frameworks

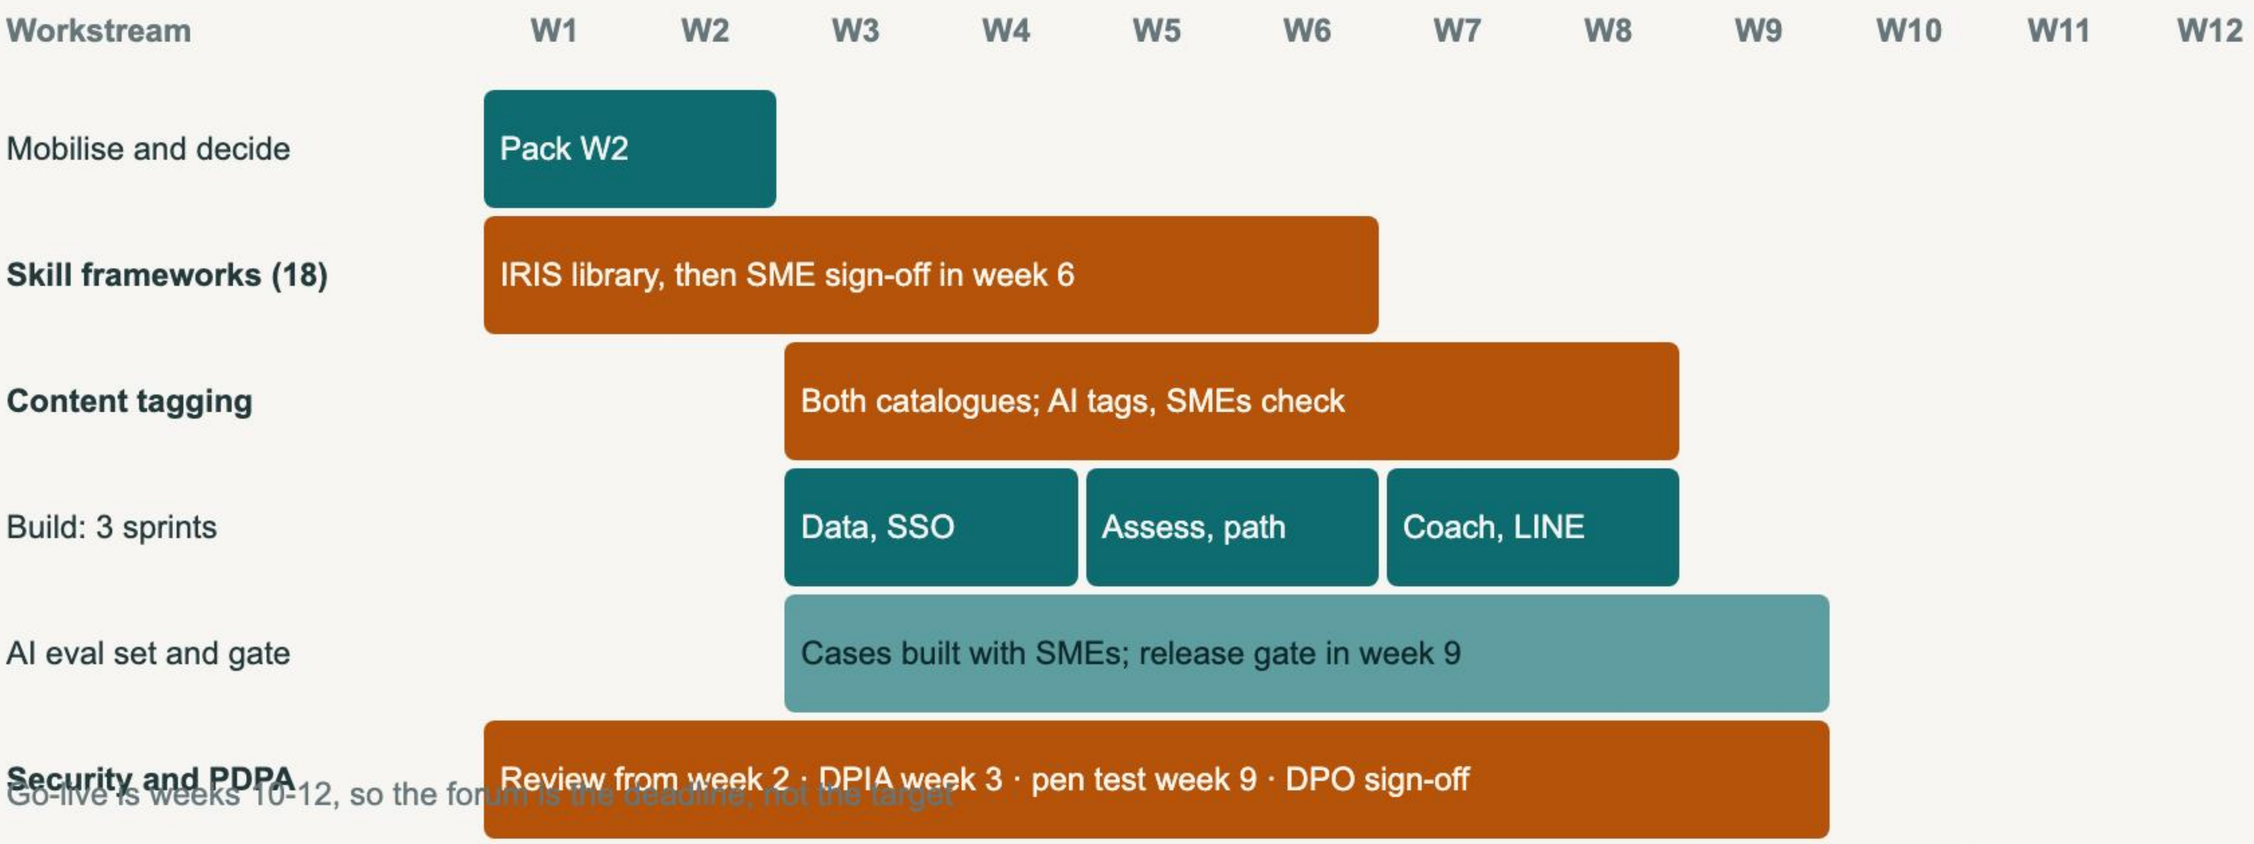

Go-live is weeks 10-12, so the forum is the deadline, not the target

The top risks have weekly review and fallbacks; scaling to 45,000 means more frameworks, not a rebuild

Risk to the date	Level	Mitigation	Fallback
Security or PDPA approval late	**High**	Pack in week 2; weekly clinic with IT security; reuse their approved cloud patterns	Security/DPO-approved reduced mode; otherwise defer employee-data use
Frameworks not agreed	**High**	Start from the IRIS library (~70% reuse); SME sign-off by week 6; version 1, then monthly updates	Sponsor-approved current-role fallback; next-role scope deferred
HR and LMS data quality	**High**	Profile data in weeks 1-2; job-code mapping table; a "wrong manager?" button; CSV fallback for LMS feeds	Approvals go to the HRBP
Scope creep across 5 BUs	**High**	Product council with the CHRO delegate; change control; a backlog for later waves	Move it to wave 2
Frontline access and adoption	**Med**	Entry through LINE; 5-minute check done in shift huddles; 60 champions; 2 h a month of paid learning time	Supervisor-led sessions on shared tablets
AI quality in Thai	**Med**	Eval gate; narrow scope; fixed replies for sensitive topics; SME review every week	Coach answers lesson content only

Wave 1 · month 4 · 12,000

RD and PK in Thailand. Prove the whole loop and set the baseline.

Wave 2 · month 7 · +15,000

BM, CS and the rest of Thailand. AI drafts frameworks from job descriptions; SMEs check them.

Wave 3 · month 13 · +18,000

Chemicals and 3 ASEAN countries: local languages, a DPIA per country, local content.

Run cost per employee falls from about THB 62 to THB 25 a month as fixed costs spread; the client's team takes over 1 quarter.

THB 15.5M to build and about THB 25 per employee a month to run; priced at THB 39 with AI included

Cost to IRIS

THB 7.3M

to build in 12 weeks: team 5.9M (14.2 average FTE; ~17 individuals), third-party 0.8M, contingency 0.6M

Run cost / employee / month	THB
12,000 staff (month 4)	62
45,000 staff (month 36)	**25**

What the run cost is made of, at 45,000

Price (recommended)

1. **Implementation:** THB 15.5M fixed, including a 10% premium for the fixed date. Paid 30 / 30 / 40.
2. **Subscription:** THB 39 per enrolled employee per month for platform, hosting, AI coach and L2 support. Minimum 20,000 from wave 2; 3-year term.
3. **Rollout per wave (fixed):** wave 2 THB 6M; wave 3 THB 9M including ASEAN localisation.
4. **10% of the subscription at risk** on adoption KPIs. Nothing tied to business KPIs until there is a baseline.

Not time-and-materials: the client would carry the date risk. Not outcome-only: there is no baseline yet.

3 years and value

THB M	Y1	Y2	Y3	Total
Client pays	29.2	30.1	21.1	**80.3**
IRIS profit	11.0	12.2	7.7	**31.0**


38.5% gross margin. Steady state is THB 468 per employee a year, 14% of today's L&D spend per head.

THB 53M


a year in value at scale, 2.5x the subscription

Workbook verified: 1,207 cached formulas · zero errors · 145 independent checks + 4 sensitivities

Hosted Clerk + Prisma stack is live; Google/LINE Login enabled; live AI release gate still open



Guardrails



Coach + lesson



Leader dashboard (illustrative data)

Current status

Mock data only: fictional company, people and courses

Hosted: **iris-learning-suite.vercel.app** (Next.js + Clerk + Prisma/Supabase). Google + LINE

Implementation and proof

Proven: hosted /api/status (Clerk + prisma+supabase); local Clerk email journeys + dual

Tools I used

Original draft: Claude Code/Cursor. Continuation: Codex & Cursor for auth, security, evals, integration,
